

Project Plan

Dormio

Industry Partner	
Primary Instructor	Laily Ajellu
Team Member	Bryan Paul Yabut
Team Member	Ibrahim Abdillahi
Team Member	Patrick Sherwin Millares
Team Member	Patrick Solamillo
Team Member	Yousuf Salihi

Document Revision History

Revision #	Date
------------	------

2.5	9/29/25
-----	---------

Table of Contents

1. Executive Summary.....	2
2. Project Approvers, Reviews and Distribution List.....	3
3. Scope.....	4
4. Deliverables.....	5
5. Assumptions.....	6
6. Dependencies.....	7
7. Risk Management.....	8
8. Communication.....	10
Meetings.....	11
9. Task Listing (WBS- Work Breakdown Structure).....	12
10. Gantt Chart.....	14
11. Milestones.....	15
12. RAM – Responsibility Assignment Matrix.....	16
13. Approval.....	17

1. Executive Summary

The following describes the project to be executed.

Objective	To design and develop an MVP of Dormio, an app with the objective of simplifying daily residence life for students by automating and centralizing their tasks, and to provide residence staff with an efficient system for maintenance management.
Corporate Goals Addressed	• Enhance student well-being and success - by centralizing management of schedules, budgets and chores, students can better focus on their academics. • Improve residence management efficiency • Deliver modern IT solutions
Planned Start Date	September 8, 2025
Planned End Date	December 12, 2025

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Project Manager	Laily Ajellu	Laily.Ajellu@georgebrown.ca	9/29/25
Developer	Bryan Paul Yabut	bryn.ybt@gmail.com	9/29/25
Developer	Ibrahim Abdillahi	ibrahimabdillahi2222@gmail.com	9/29/25
Developer	Patrick Sherwin Millares	millareslepatrick@gmail.com	9/29/25
Developer	Patrick Solamillo	PatrickSolamillo@gmail.com	9/29/25

Developer	Yousuf Salihi	salihiyousuf@gmail.com	9/29/25
-----------	---------------	------------------------	---------

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
User and Staff Documentation - Provision of user guides and technical documentation that clearly illustrate application flow, features, and system architecture	Live Payment Processing - Dormio will not process, integrate with, or initiate any online transactions.
User Management - Implementation of secure user accounts and profiles for both student and residence staff	Handling of Sensitive Information - Dormio will not store sensitive data such as financial credentials.
Customizable Meal Manager - functionality allowing students to select, save, and modify a personalized, meal plan based on preferences.	Migration of Data - there will be no automated tools to migrate existing student information into Dormio
Budget Management System - A tool for personal finance tracking, including manual transaction entry and bill splitting functionality among assigned roommates.	Third-Party Software Integration - Dormio will not integrate third-party software.
Maintenance Requests System - Allows students to submit and track maintenance requests, and enables Residence staff to manage and update request status.	Group Communication Features - features such as in-app group chat or direct messaging between residents are out of scope

4. Deliverables

This project will deliver the following.

Deliverable	Description
Project Plan	This Documentation will outline how our team will execute the project for sprint 2, including the goal, timelines, group-members task, risk management strategies giving us a solid road map to stay focused and meet deadlines.
Team Charter	Team charter defines roles and our purpose/responsibility with what needs to be done by each member. It actively helps with ensuring collaboration and communication keeping all parties accounted for their work through development.
Product Backlog	A comprehensive, prioritized list of all desired features, requirements, and enhancements for the Dormio application
Sprint Backlog	A subset of items selected from the Product Backlog, along with the team's plan for implementing them during a specific, upcoming sprint cycle.
Gnattt log Chart	A visual timeline that illustrates the project schedule, showing the planned start and end dates for all tasks (WBS) and milestones, clearly displaying dependencies.
Demonstration and Final Presentation	Demo will show the usage of our project with a detailed explanation of its design and functions.

5. Assumptions

This project makes the following assumptions;

1. **Consistent User Connectivity:** We assume student residents will have reliable and consistent internet access within the dormitories, as the app is designed to function as a centralized, real-time hub.
2. **Administrative System Adoption:** We assume the Dorm Administration team will fully adopt and integrate the new Maintenance Request System, and provide any necessary access permissions for the system to interface with residence workflows.
3. **Data Security Sufficiency:** We assume the security measures implemented are fully sufficient and compliant to adequately protect all sensitive student information, particularly financial and personal data.
4. **Positive User Engagement:** We assume the target student user group will be willing to consistently and frequently use the new app for managing daily tasks like finances and meal planning.
5. **Technical Stack Stability:** We assume the chosen technology stack will remain accessible (free or within budget) and stable throughout the development and testing lifecycle.
6. **Unchanged Project Scope:** We assume the finalized set of features and requirements will remain fixed after the initial approval, preventing any scope creep that would jeopardize the project deadline.
7. **Resource Availability:** We assume all core team members will maintain the agreed-upon availability and commitment needed to complete their assigned tasks without major unforeseen personal or academic conflicts.

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed;

1. **Database Connection & Seeding:** Our software is dependent on the population of the database. All feature functionality and testing are blocked until the database is successfully connected and populated with initial test data.
2. **Version Control System (VCS) Setup:** Our team will push to the shared Git repository so that each member is working on the latest version of the software. All collaborative coding efforts are dependent on this system being properly set up.
3. **Finalized Design Documents:** Successful implementation of features is dependent on the final sign-off of the Wireframes for all features and the Designing database schemas and relationships.
4. **Team Member Output:** Implementation of complex features is dependent on the successful completion of foundational work by other team members
5. **Administrative Access Credentials:** Final testing and deployment of the Maintenance Request System requires cooperation and the provision of necessary access credentials from the Residence Staff.
6. **Required External Approvals:** The implementation of features impacting staff (like the Maintenance Request System) is dependent on final approval and sign-off from the Residence Staff/Management on the proposed workflow and data collection.
7. **Resource Allocation:** The project timeline is dependent on all team members maintaining their commitment to the hours allocated in the RAM and Gantt chart.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Team member leaves the group	M	M	Tasks are broken up into multiple smaller tasks. These tasks are then divided up amongst remaining members. Potentially request new member.
Team member is unable to complete work by deadlines	L	L	Tasks are divided amongst other members. Participation is marked and if the issue continues it can be escalated to professor.
Scope of project is greater than previously thought.	H	M	Create a buffer of time for task completion (e.g 5 days before deadline)

			Simplify features to bare minimum required. Additional research of code libraries that may aid completion. Project plan and timeline need to be updated.
Third party service such as database becomes unavailable/paid	M	L	If database is down prevent usage of features that require database functionality . Relevant details such as meal plan are stored locally so it is still displayed when database is down and can be updated once service is fixed.
Loss of projects codes and files	H	L	Create backups regularly and create plans for team members to follow for continuous usage of the version control system.
Features work on one person's computer but not on others	M	M	Ensure that dependencies are added to version control to ensure the same dependencies are used. Environments

			such as emulators are created to be as consistent as possible according to a created project guide.
Features as described in Project Reports are not detailed enough causing unclear requirements for feature	L	L	During meetings when working on code. The full extent of the features will be discussed. What features are the focus of a meeting will be decided by the Gantt chart
Team member lacks technical knowledge required	M	M	Tasks can be divided depending on technical knowledge. Since tasks are divided by project role their partner can assist them if necessary.
Code/ Features from separate members do not work once integrated together	H	M	The structure and necessary objects will be defined early in the project. Builds will be frequently integrated(Weekly) so that any issues can be dealt with earlier on in the process.

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Project Vision	Project Manager	One-Time – (Sprint 1)
Business Requirements	Project Manager	One-Time – (Sprint 1)
Personas	Project Manager	One-Time – (Sprint 1)
User Stories	Project Manager	One-Time – (Sprint 1)
Minutes of Meeting	Project Manager	Weekly – Thursday at 1:30pm

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Meeting #1	Division of Work and approval of system features	Bryan Paul Yabut, Yousuf Salihi, Patrick Sherwin Millares, Patrick Solamillo, Ibrahim Abdailahi	Weekly – Thursday at 1:30
Meeting #2	Creation of current sprint files. Tracking pace of current work.	Bryan Paul Yabut,	Weekly – Thursday at 1:30

		Yousuf Salihi, Patrick Sherwin Millares, Patrick Solamillo, Ibrahim Abdaillahi	
Meeting #3	Division of Work for sprint 2	Bryan Paul Yabut, Yousuf Salihi, Patrick Sherwin Millares, Patrick Solamillo, Ibrahim Abdaillahi	Weekly – Thursday at 1:30
Meeting #4	Tracking current progress on sprint #2 and division of presentation responsibilities	Bryan Paul Yabut, Yousuf Salihi, Patrick Sherwin Millares, Patrick Solamillo, Ibrahim Abdaillahi	Weekly – Thursday at 1:30

9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.


Reference	Tasks	Duration	Dependency
A	Deciding on an appropriate tech stack for the application	4 hours	


B	Deciding what data needs to be stored locally and, on the database,	5 hours	A
C	Designing and creation of user roles and permissions in the system	8 hours	B
D	Creation of wireframes for all features (Admin site & Mobile app)	3 days	C
E	Designing database schemas and relationships between tables in a SQL RDBMS	2 days	D
F	Setting up database connection and seeding initial data	1 day	E
G	Setting up GitHub repositories and initializing the project for both Admin site and Mobile app	4 hours	
H	Implementation of CRUD operations for all features based on user roles	5 days	F
I	Implement simplified interactions and UI design for user features (Admin site)	6 days	H
J	Designing the mobile app UI	4 days	H
K	Implementation of data visualization for the Budget Management System	1 day	J
L	Implementation of scheduling, meal planning, and maintenance request features with logic to restrict choices	7 days	K
M	Implementation of Chore Manager and CSV export logic	3 days	L
N	Implementing REST API connection and integrating it to the Mobile app	6 days	J, K, L, M

O	Integrate and test all implemented features into a unified dashboard	3 days	N
P	Final testing and debugging	5 days	P

10. Gantt Chart

[Link: Dormio Gantt chart PDF](#)

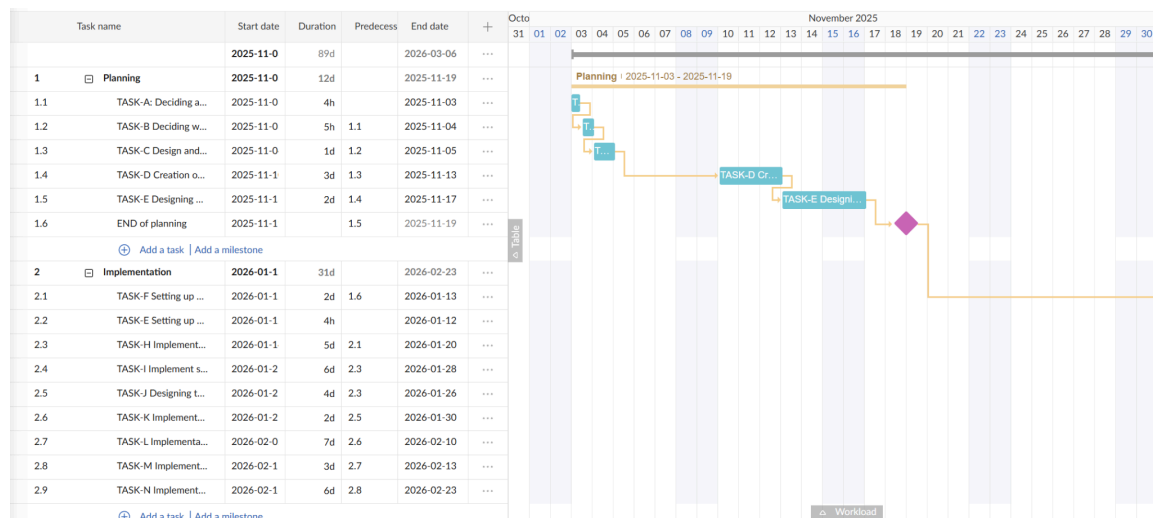

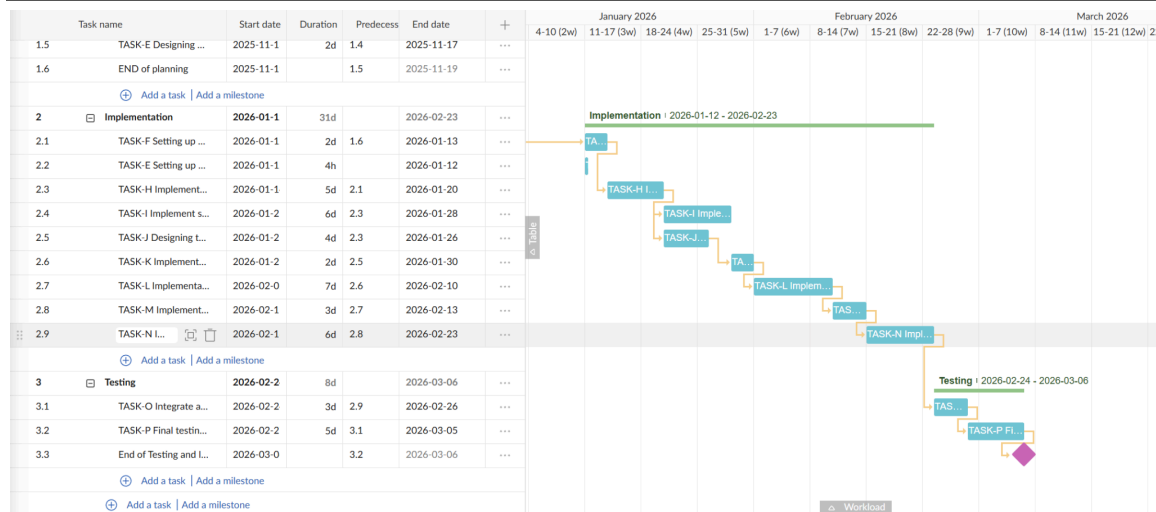

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Deciding on tech stack finalized	November 3, 2025	Bryan Paul Yabut, Patrick Sherwin Millares
Data storage structure planned (local vs database)	November 4, 2025	Ibrahim Abdillahi, Bryan Paul Yabut
User roles and permissions completed	November 5, 2025	Patrick Solamillo, Ibrahim Abdillahi
Wireframes created for Admin site and Mobile app	November 13, 2025	Yousuf Salihi, Patrick Sherwin Millares
Database schema and relationships finalized	November 17, 2025	Ibrahim Abdillahi

Database connection setup and seeded	January 13, 2026	Patrick Sherwin Millares
GitHub repository setup and project initialized	January 12, 2025	Bryan Paul Yabut
CRUD operations implemented	January 20, 2026	Team
Admin site UI simplified and designed	January 28, 2026	Patrick Sherwin Millares, Yousuf Salihi
Mobile app UI completed	January 26, 2026	Yousuf Salihi
Budget Management data visualization added	January 30, 2026	Yousuf Salihi
Scheduling, meal planning, and maintenance request features implemented	February 10, 2026	Patrick Sherwin Millares, Ibrahim Abdillahi
Chore Manager and CSV export completed	February 13, 2026	Bryan Paul Yabut, Patrick Solamillo
REST API integrated with mobile app	February 23, 2026	Yousuf Salihi, Patrick Sherwin Millares
Unified dashboard integration	February 26, 2026	Team
Final testing and debugging	February 05, 2026	Team
Final presentation and demo	March 06, 2026	Team

12. RAM – Responsibility Assignment Matrix

Create a RAM from your Task Listing. A sample is shown below:

Project Team Responsibilities

Project Name:	Dormio				
Project Manager:	Laily Ajellu				
Task	Bryan Paul Yabut	Ibrahim Abdillahi	Patrick Sherwin Millares	Patrick Solamillo	Yousuf Salihi
Deciding on appropriate tech stack	P		S		
Deciding what data needs to be stored locally and on the database	S	P			
Designing and creating user roles & permissions		P		S	
Creating wireframes for Admin site & Mobile app			S		P
Designing database schema & relationships		P	S		
Setting up database connection & seeding data		S	P		
Setting up GitHub repositories & initializing project	P			S	
Implementing CRUD operations for all features	S	S	P	S	
Implementing simplified Admin UI			P		S
Designing Mobile App UI			S		P
Implementing Budget Management visualization					P
Implementing scheduling, meal planning & maintenance features		S	P		
Implementing Chore Manager & CSV export	P			S	
REST API integration with Mobile app			P		S
Integrate & test all features into a unified dashboard	S	S	P	S	S
Final testing & debugging	S	S	S	S	P
P = Primary (Responsible) S = Secondary (Support)					

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Developer	Yousuf Salihi		10/25/2025
Developer	Patrick Solamillo		10/25/2025
Developer	Bryan Paul Yabut		10/25/2025

Developer	Patrick Millares		1-/25/2025
Developer	Ibrahim Abdillahi		1-/25/2025
